


754 Alhambra

CVSAN\_2304 Combination of two previous jobs....C&E ~262 ft total  
CVSAN\_C Project Details Full line replacement by pipe burst. 8" VCP, 125 ft MH-MH in sidewalk, steep incline.

Contractor responsible to verify all dimensions, descriptions and conditions.

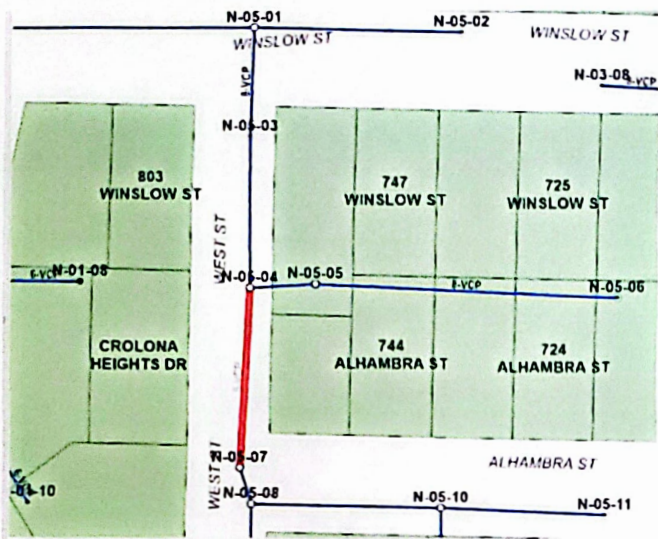

Previous suspected lateral problem at 754 Alhambra may be related. Lower MH 3.3', upper MH 4.5' invert depth

Details CVSan 23E 8" VCP, 60 ft from N-05-03 to N-05-01, RI to MH, Pipe burst. could Repair lower portion 15' but this segment has breakin tap and also is location of seep spring at West and Wnslow.

N-05-01 is 6' invert depth, N-05-03(rod inlet) is 4' invert depth, s

Note incorrect numbering on screenshot

Contractor to verify all conditions

